

WRC July 2023

Capital Programme and Asset Management Update

Reliance Street HWRC





Background and site restrictions

- Older asset, not previously developed ,
- Small footprint,
- Restrictive access,
- Limited recycling ability
- Limited traffic volumes and local impact
- Operational disruption



HWRC

Redundant Anaerobic
Digestion (AD) Plant


TLS

Reliance Street
Household Waste and...

Mechanical Treatment
and Reception Building
(MTR)

SUEZ recycling
and recovery UK

Reliance Street

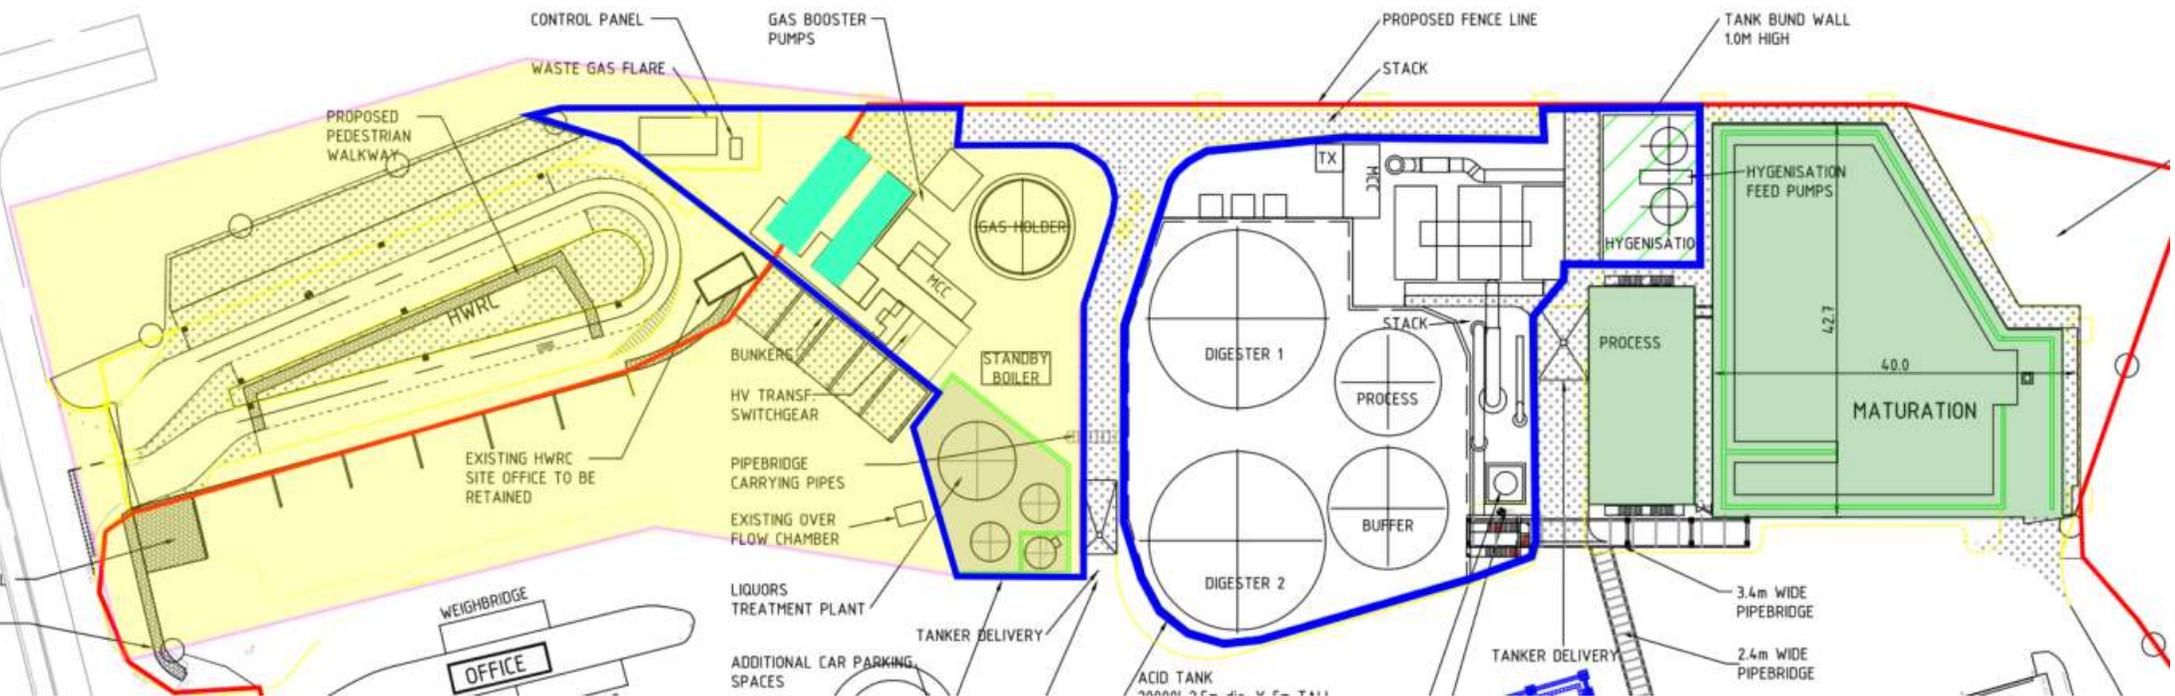

Current Position

- Planning decision granted in February 2023
- Enabling works and service disconnections actioned Jan – May 2023
- Anaerobic Digestion (AD) tanks and equipment demolition – May – July 2023
- Ground Investigations – Geotechnical review
- Finalisation of design and specification

Demolition

- Phase 1 – Complete
- Phase 2 – Ongoing (completed July- August)





Delivery

- Conclude demolition
- Complete design and specification
- Procurement and contractor appointment
- Planning conditions – Pre-commencement
- Construction – Target start mid- March 24
